HJMU–112
(MU–103)

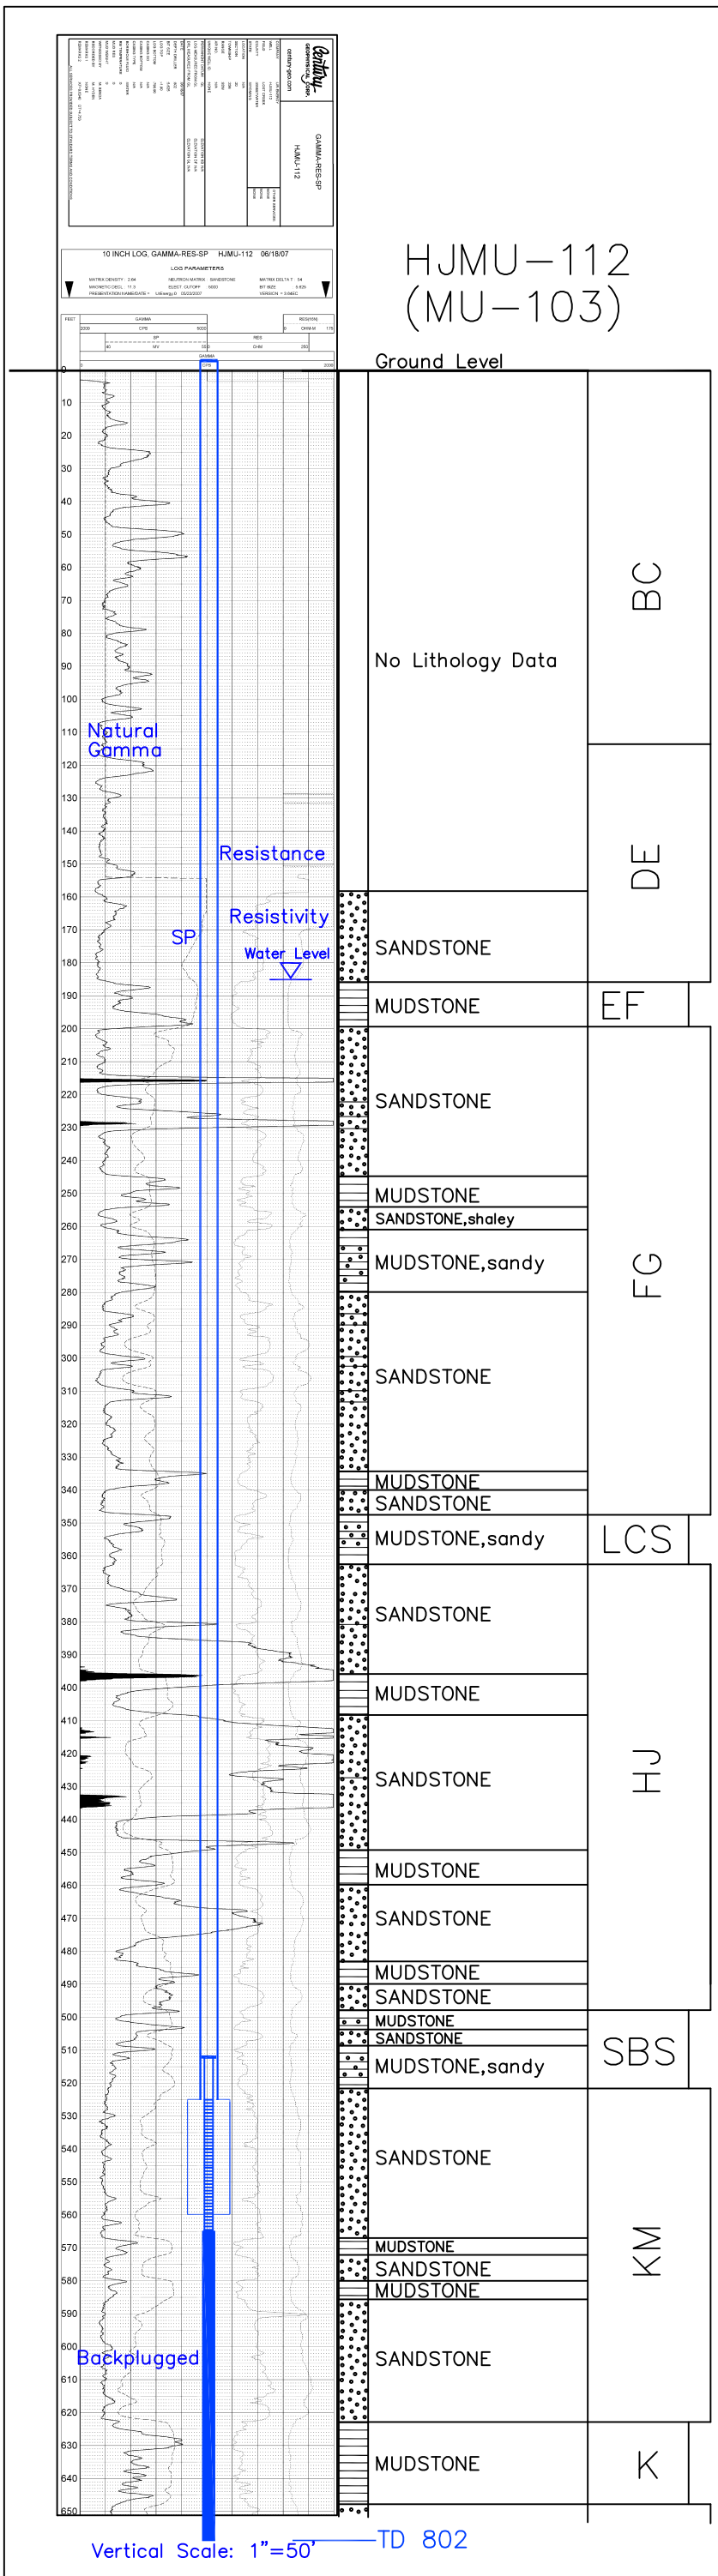

Lost Creek ISR, LLC

WELL COMPLETION REPORT

WELL # HJMU–112 SEO # 179896 Date Drilled: 6–18–07

Location: E 744,386 / N 534,676 (NAD 27)

Ground Elev: 6934.18' Measure Point Elev: 6935.35'

TD: 802' Hole Dia.: 7–7/8"

CASED to: 525' Casing: PVC SDR17 ID: 4.5" OD: 5"

GROUT: Portland Cement – Type I/II
Pumped thru casing, displaced to surface with water

COMPLETION Aquifer: UKM Sand

Static Water Level: Depth 185' Elev: 6750' (avg.)

UNDERREAM: Blade Dia: 10.5"

Intervals: from 525' to 560' /length 35'

from _____ to _____ /length _____

SCREEN LINER ASSEMBLY

Description	Depth From	– To	Elev. / From	– To	Length
K–packer		512'		6423'	
Screen	525'	565'	6410'	6370'	40'

SCREEN SPECIFICATIONS:

Slot: 0.030" Composition 3" PVC

FILTER PACKING:

Volume: _____ (bags)(ft^3) Sand Specs. _____

Method: N/A

WELL STIMULATION: Method Airlift

Yield: (Good) / Moderate / Poor

Pilot Hole BACKPLUGGED: 565'–802'

w/ BH Ultragrout slurry – 25% solids

HJMU–112
(MU–103)
