HJMU–107
(MU–104)

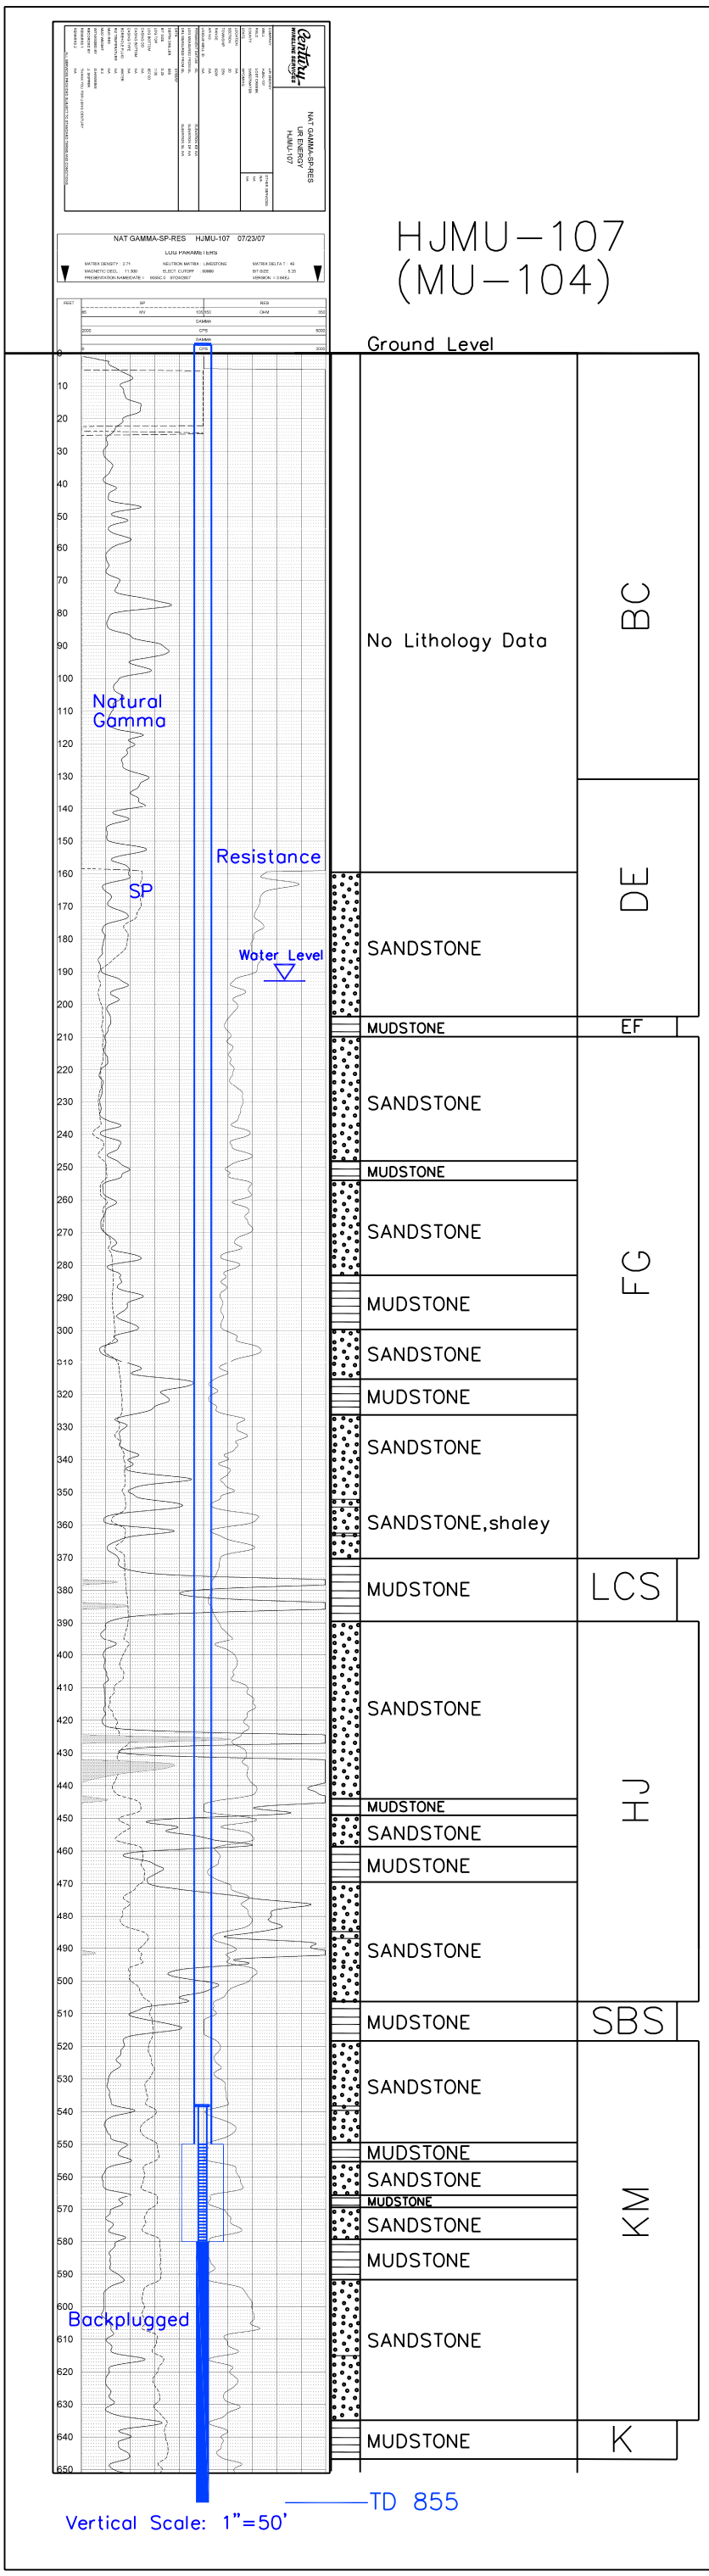

Lost Creek ISR, LLC

WELL COMPLETION REPORT

WELL # HJMU–107 SEO # 179881 Date Drilled: 7–23–07

Location: E 743,686 / N 534,788 (NAD 83)

Ground Elev: 6936.84 Measure Point Elev: 6937.88

TD: 855 ft. Hole Dia.: 7–7/8"

CASED to: 550' Casing: PVC SDR17 ID: 4.5" OD: 5"

GROUT: Portland Cement – Type I/II
Pumped thru casing, displaced to surface with water

COMPLETION Aquifer: UKM Sand

Static Water Level: Depth 193' Elev: 6745'

UNDERREAM: Blade Dia: 10–1/2"
Intervals: from 550' to 580' /length 30'
from _____ to _____ /length _____

SCREEN LINER ASSEMBLY

Description	Depth From	– To	Elev. / From	– To	Length
K–packer		538'		6399	
Screen	550'	580'	6387'	6357'	30'

SCREEN SPECIFICATIONS:
Slot: 0.030" Composition 3" PVC

FILTER PACKING:
Volume: _____ (bags)(ft^3) Sand Specs. _____
Method: N/A

WELL STIMULATION: Method Airlift
Yield: Good / Moderate / Poor

Pilot Hole BACKPLUGGED: 580'–855'
w/ BH Ultragrout slurry – 25% solids

HJMU–107
(MU–104)
