Lost Creek ISR, LLC

WELL COMPLETION REPORT

MB–07

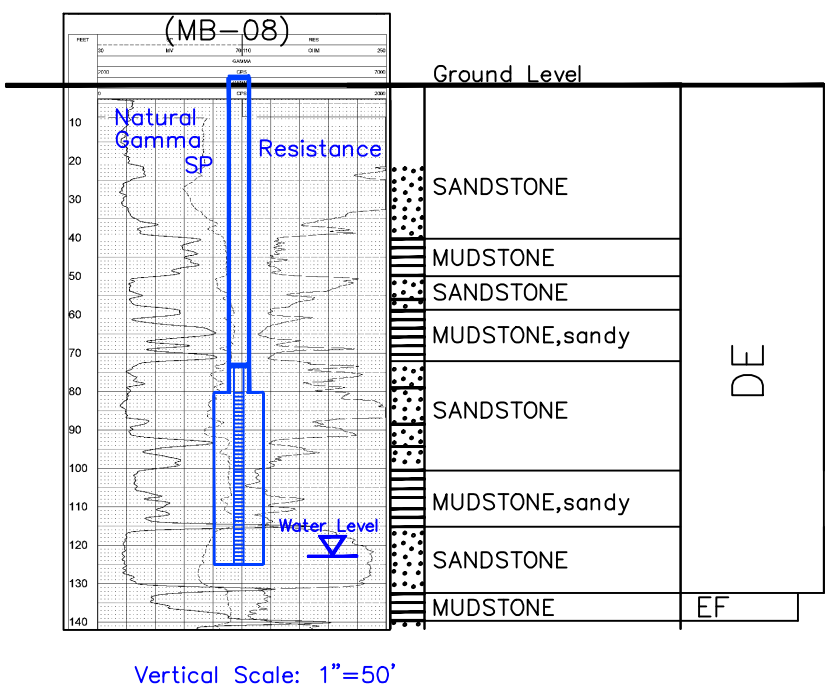

NOTE: MB–07 was drilled with air. Hole made no water. Hole not logged. Log for MB–08 used here as representative.

WELL # MB–07 SEO # 188858 Date Drilled: 10–22–08

Location: E 753,266 / N 538,981 (NAD 27)

Ground Elev: 6983.38 Measure Point Elev: 6984.88

TD: 140 ft. Hole Dia.: 7–7/8"

CASED to: 80' Casing: PVC SDR17 ID: 4.5" OD: 5"

GROUT: Portland Cement – Type I/II
Pumped thru casing, displaced to surface with water

COMPLETION Aquifer: DE Sand

Static Water Level: Depth 123' Elev: 6861' (typical)

UNDERREAM: Blade Dia: 10–1/2"

Intervals: from 80' to 125' /length 45'

from _____ to _____ /length _____

SCREEN LINER ASSEMBLY

Description	Depth From – To		Elev. From – To		Length
K–packer		73'		6911'	
Screen	80'	125'	6904'	6859'	45'

SCREEN SPECIFICATIONS:
Slot: 0.020" Composition 3" PVC

FILTER PACKING:
Volume: _____ (bags)(ft^3) Sand Specs. _____
Method: N/A

WELL STIMULATION: Method Airlift
Yield: Good / Moderate / Poor
